

Kurchi Projects

Every item, from the factory floor to an installed showroom, carries a known status, a known owner and a photo trail — shown to the people who need it and hidden from everyone else.

5 roles

19 item states

60+ business rules


6 build phases

Ola showroom roll-out · pilot

CONTENTS		DOCUMENT	
01	Mind map — the whole system on one page	PREPARED FOR	Kurchi — Ola showroom roll-out
02	Five roles, five different apps	DATE	21 September 2026
03	The journey of one chair, and what damage costs	STATUS	Blueprint v1 — three decisions locked, six questions open
04	What the system will not let you do	FULL SPEC	kurchi-projects/docs — 7 documents
05	Pages by role	Internal — contains cost and margin structure. Not for circulation to the client.	
06	Seven additions worth building first		
07	Settled, and still open		

Mind map

Six territories. The left half is what you set up once; the right half is what happens on every project.

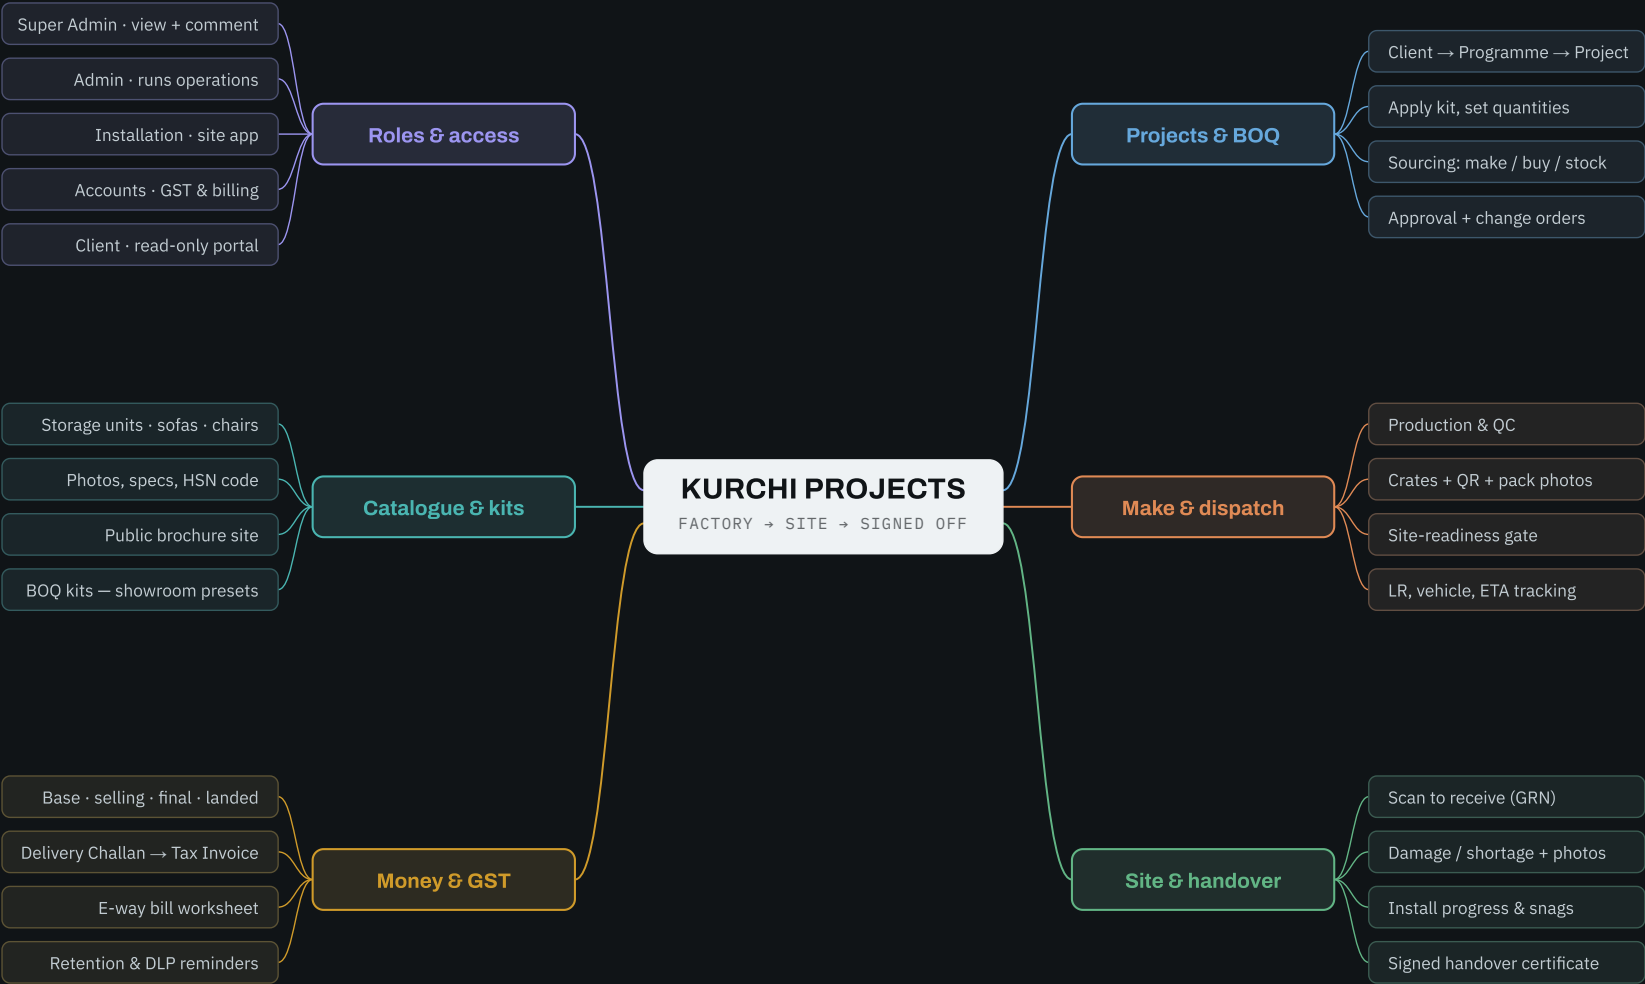


Five roles, five different apps

Same data, five views. What a role cannot see matters as much as what it can — the client must never see cost or margin, and the installer must never see any price at all.

Super Admin /hq • All graphs: revenue, margin, delays • Every project, every city • Rework cost by cause • Vendor & team scorecards • Comments on anything Cannot edit a single field. Oversight without interference.	Admin /admin • Creates projects from kits • BOQ, sourcing, all four price fields • Production, QC, packing, dispatch • Triage damage, approves replacements • Users, catalogue, vendors Cannot issue invoices or edit an approved BOQ in place.	Installation /site • Phone-first, works offline • Scan crate QR to receive • Reports damage with photos • Daily install progress • Raises and closes snags Cannot see any price, cost or vendor name.	Accounts /accounts • Delivery Challans (bill-to / ship-to) • E-way bill worksheet • Tax invoices, CGST/SGST vs IGST • Payments, ageing, vendor bills • GSTR-1 shaped export Cannot change BOQ, production or site data.	Client /portal • Live progress per showroom • Scope at selling price only • Consignment ETAs • Approves BOQ & change orders • Signs handover with OTP Cannot see cost, margin, vendor or internal notes.
--	---	---	---	--

The journey of one chair

Every BOQ line carries its own status. This is what makes “where is my chair” answerable without a phone call. Dashed boxes are gates — the system refuses to move past them.

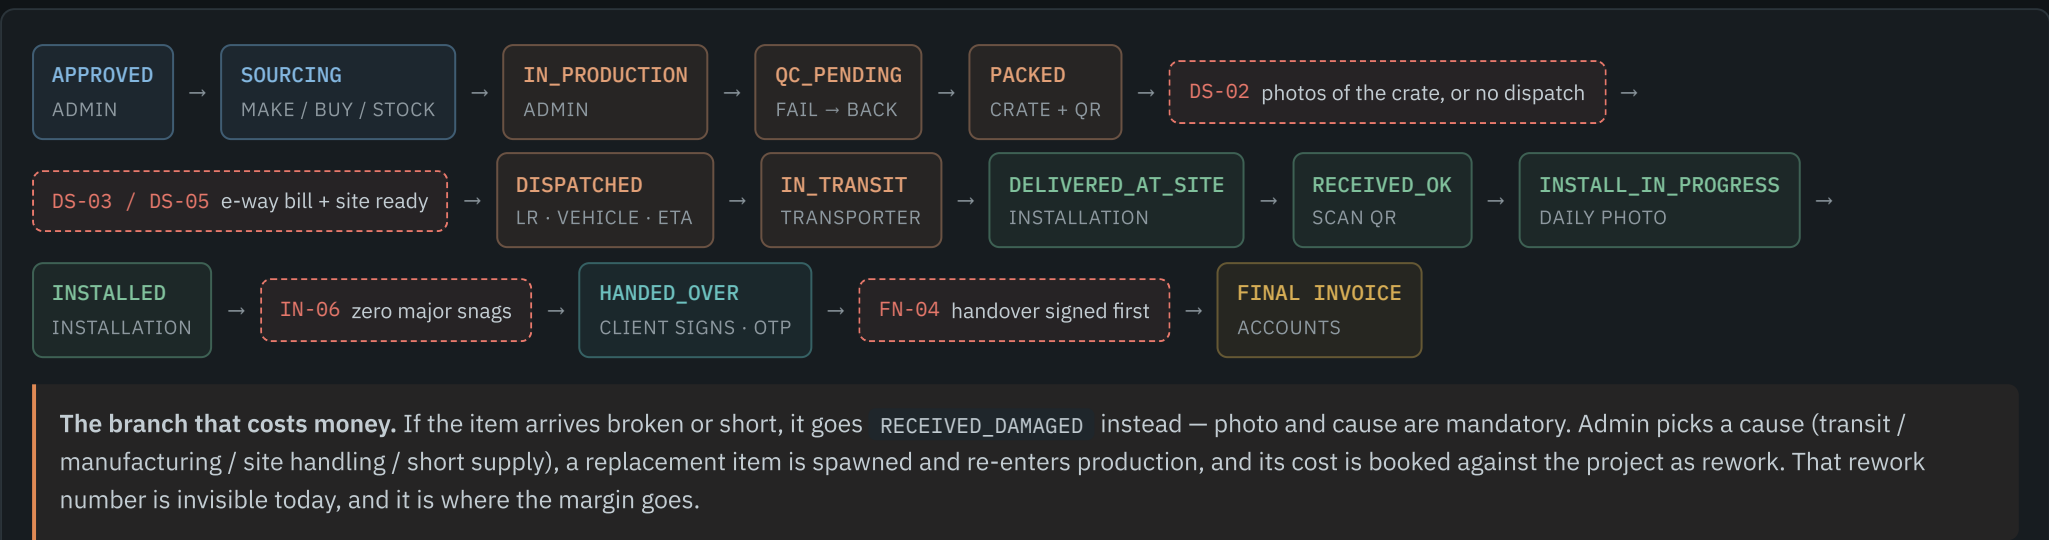

What that one cracked chair leg actually cost

Six chairs, one damaged in transit. “Actual price” = landed cost: base + transport + installation + rework.

Revenue — 6 × final price ₹5,400	₹32,400
Base price — 6 × ₹3,200	₹19,200
Allocated transport	₹1,800
Allocated installation	₹1,200
Rework — the replacement chair	₹3,200
Landed cost — the “actual price”	₹25,400
Quoted margin — what we expected	₹13,200
Real margin — what we made	₹7,000
Erosion	₹6,200 — 47% gone

04 — THE IF / ELSE THAT MATTERS

What the system will not let you do

These are workflow gates, not permissions. Even Admin cannot pass them without a typed reason, and every override lands on the Super Admin dashboard. Full catalogue of 60+ rules lives in `docs/02-workflow.md` .

RULE	IF...	THEN THE SYSTEM	UNBLOCKED BY
DS-02	Crate has zero packing photos	blocks dispatch	Upload photos
DS-03	Value > ₹50,000 or inter-state, no e-way bill	blocks dispatch	Accounts enters e-way bill no.
DS-05	Site readiness not all green	blocks dispatch	Site confirms, or Admin override + reason
ST-01	Qty received < qty dispatched	auto-raises a shortage ticket	Replacement or waiver
ST-02	Damage reported with no photo	rejects the report	Attach photo + pick a cause
ST-03	Open damage ticket on an item	blocks “Installed”	Close or supersede the ticket
IN-06	Any major or critical snag open	blocks handover	Close snags, or client waiver
FN-04	Handover not signed	blocks the final invoice	Client signs with OTP
PR-03	BOQ already approved	refuses in-place edits	Raise a change order
FN-07	Invoice already issued	refuses any edit	Issue a credit note
ES-01	Item status unchanged past its SLA	flags it stale on two dashboards	Move the item, or put project on hold
AC-01	Super Admin attempts any write	rejects, except comments	Nothing — that is the role

Pages by role

One login at `/login` , then routed by role. Filter to see one role's world.

Public site

`/` · `/products` · `/login`

- Home + category tiles
- Catalogue: storage, sofas, chairs
- Product detail with specs
- Contact / enquiry form
- Single login, routed by role

Super Admin

`/hq`

- Command centre: 7 charts
- Attention tiles: delays, stale, overrides
- All projects table
- Programme & project P&L
- Vendor + team performance

Admin — setup

`/admin/clients` · `programmes` · `kits`

- Clients & contacts
- Programmes (the Ola roll-out)
- BOQ kits, versioned
- Catalogue CRUD + HSN
- Vendors & installation teams
- Users & roles

Admin — project workspace

`/admin/projects/:id`

- Summary · BOQ · Sourcing
- Packing · Dispatch · Site
- Installation · Change orders
- Documents · Finance · Audit
- Cross-project dispatch board
- Damage & shortage queue

Installation

`/site`

- My sites
- Incoming consignments + ETA
- Scan to receive, mark OK / damaged
- Install checklist by zone
- Snags in and out
- Request handover

Accounts

`/accounts`

- Delivery challans
- E-way bill worksheet
- Tax invoices + credit notes
- Payments & ageing
- Vendor bills, 3-way check
- Retention queue · GST export

Client portal

`/portal`

- All my showrooms, health dot
- Progress + site photos
- Scope at selling price
- Deliveries & ETAs
- Approvals queue
- Sign handover · documents

06 — NOT IN THE ORIGINAL BRIEF

Seven additions worth building first

These are not decoration. Each one closes a specific hole that is costing money or causing the complaints today.

01

BOQ kits — showroom presets

Fifty near-identical showrooms. Clone a kit, adjust quantities, done. Project setup goes from hours to two minutes, and copy-paste errors disappear.

02 **Crate-level tracking with QR labels**

“Something did not arrive” is unanswerable at item level. Pack into crates, print a QR sticker, scan at dispatch and at site. Now you know *which crate*.

03 **Mandatory photos at packing and at receipt**

Settles every “it was already broken” argument, and tells you whether to claim from the transporter or fix the factory.

04 **Delivery Challan before Tax Invoice**

Goods move to site before the sale. Under GST that is a challan, not an invoice — with bill-to Ola HQ and ship-to the showroom. Getting this wrong invites notices.

05 **Site-readiness gate before dispatch**

Shipping to a site where flooring is not done means goods sit in a corridor and get damaged. Six checkboxes prevent the most expensive failure mode you have.

06 **Stale-status escalation**

If an item has not moved past its SLA, it surfaces automatically on two dashboards. Delay gets found in three days instead of three weeks.

07 **Replacement loop with costed rework**

A damaged item spawns a linked replacement that re-enters production and books its cost to the project, by cause. This is the silent margin killer made visible.

Three decisions are locked and written into the spec. The rest still need ten minutes with Kurchi.

DECIDED · PRICING

“Actual price” = landed cost. Four fields: base, selling, final agreed, and computed landed cost. Quoted margin and real margin both stored — the gap between them is the headline number.

DECIDED · CLIENT ACCESS

Full portal in v1, with BOQ approval, change orders and OTP handover signing. Field-level masking becomes a launch blocker, not later hardening.

DECIDED · GST

Generate + export. GST-correct challans and invoices, a complete e-way bill worksheet, GSTR-1-shaped export. No GSP subscription; the API route stays open.

OPEN · CLIENT USERS

Which Ola people get logins? One programme-level PM across all cities, or a site contact per showroom who only sees their own? Decides the user scoping model.

OPEN · INSTALLERS

Third-party vendors or your own staff? Decides whether the site app must be hardened for outsiders or can stay simple and trusting.

OPEN · ACCOUNTING

Is Tally or Zoho already running? If yes, the invoice number series must match theirs and this app exports rather than competes.

OPEN · CONTRACT

Retention % and DLP months? Assumed 5% and 12 months. And is billing milestone-based — advance, dispatch, completion — or one final invoice?

OPEN · STOCK

Do you hold finished stock? Or is everything made or bought per project? Decides whether a real inventory module is needed alongside make / buy.

OPEN · LANGUAGE

Hindi or regional language on the site app? Installers in tier-2 and tier-3 cities may not read English comfortably. Cheap now, painful to retrofit.

Full specification in `kurchi-projects/docs/` — overview, roles & permissions, workflow & 60+ business rules, screens, Firestore data model, roadmap, open questions. Stack: Vite · React · TypeScript · Tailwind · shadcn/ui · Firebase, matching `smart-furnish` and `ecommerce`.
