

# Kurchi Projects

Every item, from the factory floor to an installed showroom, carries a known status, a known owner and a photo trail — shown to the people who need it and hidden from everyone else.

5 roles

19 item states

60+ business rules


6 build phases

Ola showroom roll-out · pilot

| CONTENTS |                                                 | DOCUMENT                                                                          |                                                           |
|----------|-------------------------------------------------|-----------------------------------------------------------------------------------|-----------------------------------------------------------|
| 01       | Mind map — the whole system on one page         | PREPARED FOR                                                                      | Kurchi — Ola showroom roll-out                            |
| 02       | Five roles, five different apps                 | DATE                                                                              | 21 September 2026                                         |
| 03       | The journey of one chair, and what damage costs | STATUS                                                                            | Blueprint v1 — three decisions locked, six questions open |
| 04       | What the system will not let you do             | FULL SPEC                                                                         | kurchi-projects/docs — 7 documents                        |
| 05       | Pages by role                                   | Internal — contains cost and margin structure. Not for circulation to the client. |                                                           |
| 06       | Seven additions worth building first            |                                                                                   |                                                           |
| 07       | Settled, and still open                         |                                                                                   |                                                           |

# Mind map

Six territories. The left half is what you set up once; the right half is what happens on every project.

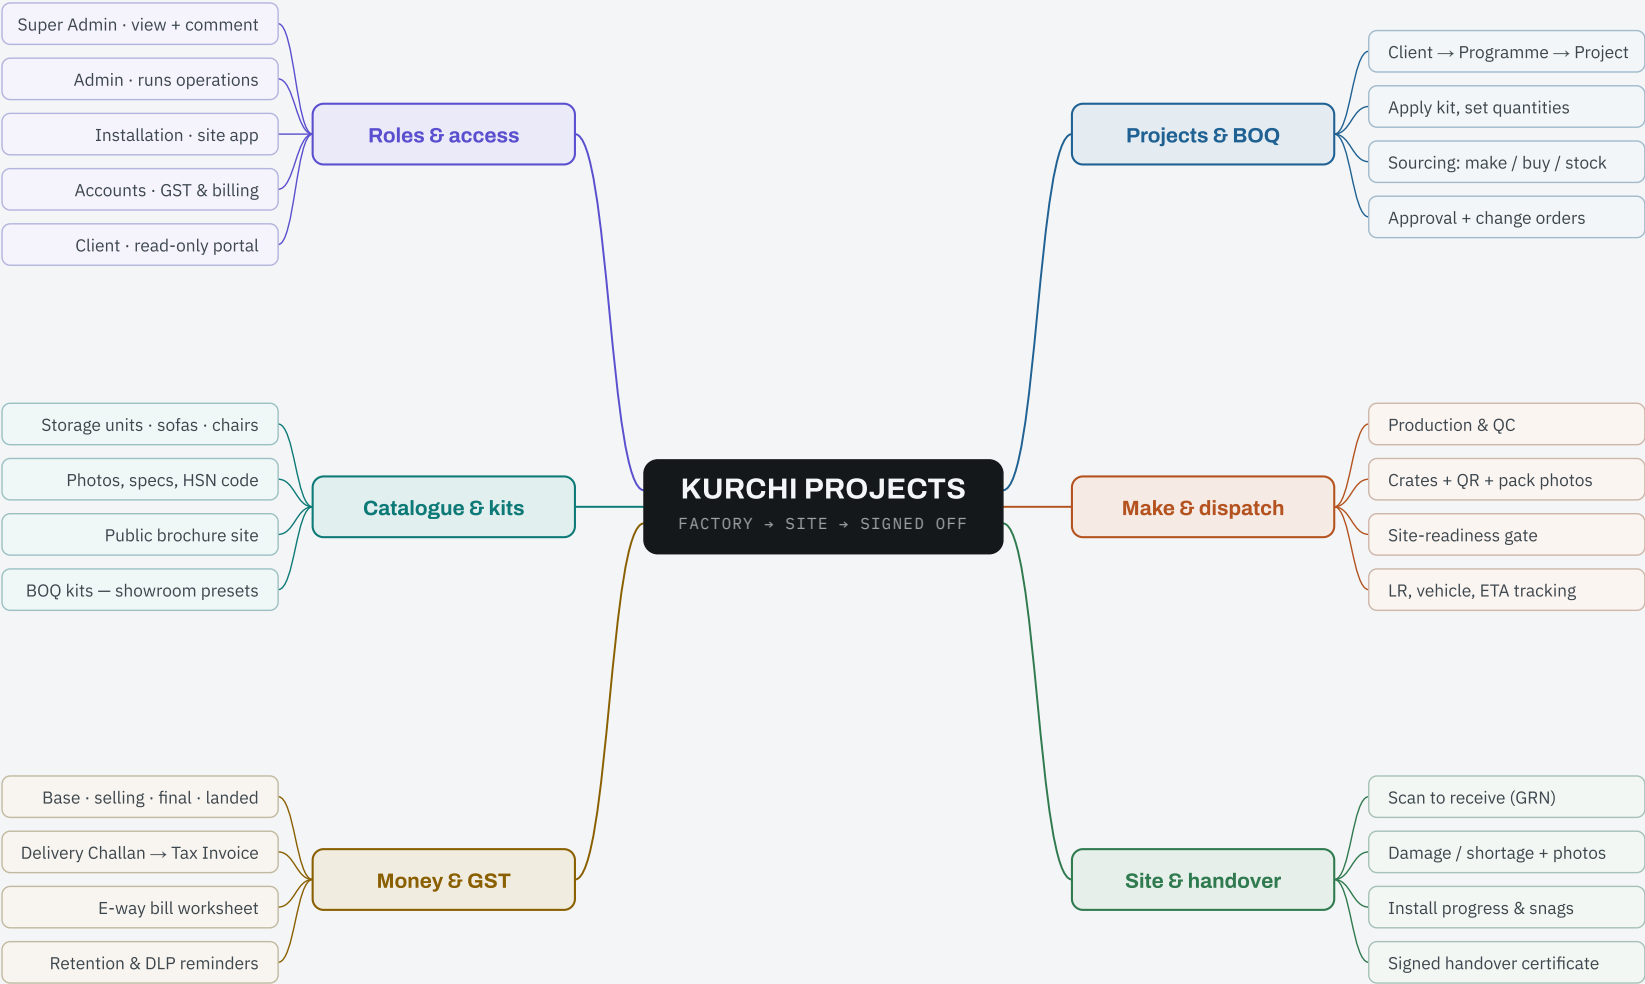


# Five roles, five different apps

Same data, five views. What a role cannot see matters as much as what it can — the client must never see cost or margin, and the installer must never see any price at all.

|                                                                                                                                                                                                                                                                                                                                                                              |                                                                                                                                                                                                                                                                                                                                                                                                |                                                                                                                                                                                                                                                                                                                                                     |                                                                                                                                                                                                                                                                                                                                                                       |                                                                                                                                                                                                                                                                                                                                                            |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <div><div>Super Admin</div><div>/hq</div><div><ul style="list-style-type: none"><li>• All graphs: revenue, margin, delays</li><li>• Every project, every city</li><li>• Rework cost by cause</li><li>• Vendor &amp; team scorecards</li><li>• Comments on anything</li></ul></div><div><div>Cannot</div>edit a single field.<br/>Oversight without interference.</div></div> | <div><div>Admin</div><div>/admin</div><div><ul style="list-style-type: none"><li>• Creates projects from kits</li><li>• BOQ, sourcing, all four price fields</li><li>• Production, QC, packing, dispatch</li><li>• Triages damage, approves replacements</li><li>• Users, catalogue, vendors</li></ul></div><div><div>Cannot</div>issue invoices or edit an approved BOQ in place.</div></div> | <div><div>Installation</div><div>/site</div><div><ul style="list-style-type: none"><li>• Phone-first, works offline</li><li>• Scan crate QR to receive</li><li>• Reports damage with photos</li><li>• Daily install progress</li><li>• Raises and closes snags</li></ul></div><div><div>Cannot</div>see any price, cost or vendor name.</div></div> | <div><div>Accounts</div><div>/accounts</div><div><ul style="list-style-type: none"><li>• Delivery Challans (bill-to / ship-to)</li><li>• E-way bill worksheet</li><li>• Tax invoices, CGST/SGST vs IGST</li><li>• Payments, ageing, vendor bills</li><li>• GSTR-1 shaped export</li></ul></div><div><div>Cannot</div>change BOQ, production or site data.</div></div> | <div><div>Client</div><div>/portal</div><div><ul style="list-style-type: none"><li>• Live progress per showroom</li><li>• Scope at selling price only</li><li>• Consignment ETAs</li><li>• Approves BOQ &amp; change orders</li><li>• Signs handover with OTP</li></ul></div><div><div>Cannot</div>see cost, margin, vendor or internal notes.</div></div> |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|

# The journey of one chair

Every BOQ line carries its own status. This is what makes “where is my chair” answerable without a phone call. Dashed boxes are gates — the system refuses to move past them.

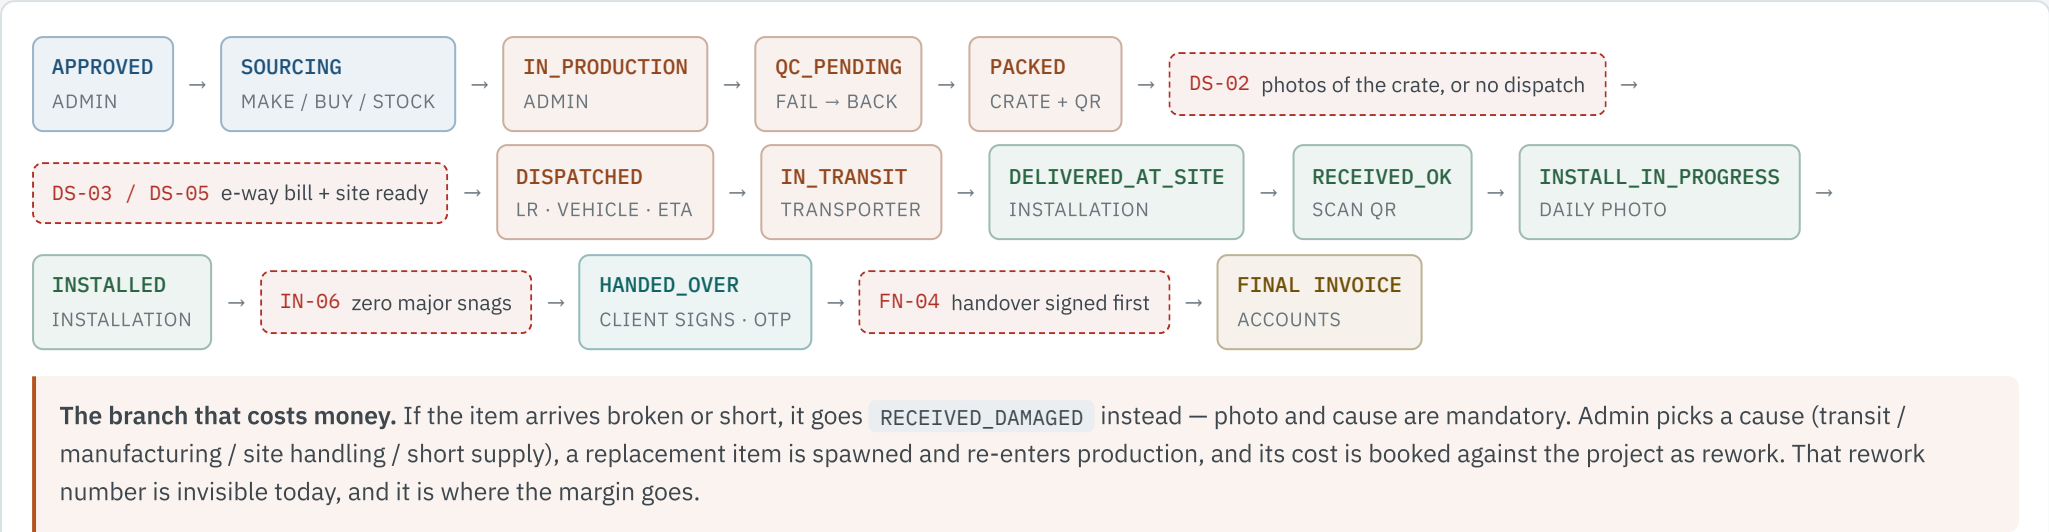

### What that one cracked chair leg actually cost

Six chairs, one damaged in transit. “Actual price” = landed cost: base + transport + installation + rework.

|                                         |                          |
|-----------------------------------------|--------------------------|
| Revenue — 6 × final price ₹5,400        | ₹32,400                  |
| Base price — 6 × ₹3,200                 | ₹19,200                  |
| Allocated transport                     | ₹1,800                   |
| Allocated installation                  | ₹1,200                   |
| Rework — the replacement chair          | ₹3,200                   |
| <b>Landed cost — the “actual price”</b> | <b>₹25,400</b>           |
| Quoted margin — what we expected        | ₹13,200                  |
| <b>Real margin — what we made</b>       | <b>₹7,000</b>            |
| <b>Erosion</b>                          | <b>₹6,200 — 47% gone</b> |

## What the system will not let you do

These are workflow gates, not permissions. Even Admin cannot pass them without a typed reason, and every override lands on the Super Admin dashboard. Full catalogue of 60+ rules lives in `docs/02-workflow.md` .

| RULE  | IF...                                         | THEN THE SYSTEM                  | UNBLOCKED BY                              |
|-------|-----------------------------------------------|----------------------------------|-------------------------------------------|
| DS-02 | Crate has zero packing photos                 | blocks dispatch                  | Upload photos                             |
| DS-03 | Value > ₹50,000 or inter-state, no e-way bill | blocks dispatch                  | Accounts enters e-way bill no.            |
| DS-05 | Site readiness not all green                  | blocks dispatch                  | Site confirms, or Admin override + reason |
| ST-01 | Qty received < qty dispatched                 | auto-raises a shortage ticket    | Replacement or waiver                     |
| ST-02 | Damage reported with no photo                 | rejects the report               | Attach photo + pick a cause               |
| ST-03 | Open damage ticket on an item                 | blocks “Installed”               | Close or supersede the ticket             |
| IN-06 | Any major or critical snag open               | blocks handover                  | Close snags, or client waiver             |
| FN-04 | Handover not signed                           | blocks the final invoice         | Client signs with OTP                     |
| PR-03 | BOQ already approved                          | refuses in-place edits           | Raise a change order                      |
| FN-07 | Invoice already issued                        | refuses any edit                 | Issue a credit note                       |
| ES-01 | Item status unchanged past its SLA            | flags it stale on two dashboards | Move the item, or put project on hold     |
| AC-01 | Super Admin attempts any write                | rejects, except comments         | Nothing — that is the role                |

## Pages by role

One login at `/login` , then routed by role. Filter to see one role's world.

|                                                                                                                                                                                                                                                                                                                         |                                                                                                                                                                                                                                                                                                                             |                                                                                                                                                                                                                                                                                                                                                            |                                                                                                                                                                                                                                                                                                                                                                             |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <div><b>Public site</b></div> <div><code>/ · /products · /login</code></div> <div><ul style="list-style-type: none"><li>• Home + category tiles</li><li>• Catalogue: storage, sofas, chairs</li><li>• Product detail with specs</li><li>• Contact / enquiry form</li><li>• Single login, routed by role</li></ul></div> | <div><b>Super Admin</b></div> <div><code>/hq</code></div> <div><ul style="list-style-type: none"><li>• Command centre: 7 charts</li><li>• Attention tiles: delays, stale, overrides</li><li>• All projects table</li><li>• Programme &amp; project P&amp;L</li><li>• Vendor + team performance</li></ul></div>              | <div><b>Admin — setup</b></div> <div><code>/admin/clients · programmes · kits</code></div> <div><ul style="list-style-type: none"><li>• Clients &amp; contacts</li><li>• Programmes (the Ola roll-out)</li><li>• BOQ kits, versioned</li><li>• Catalogue CRUD + HSN</li><li>• Vendors &amp; installation teams</li><li>• Users &amp; roles</li></ul></div> | <div><b>Admin — project workspace</b></div> <div><code>/admin/projects/:id</code></div> <div><ul style="list-style-type: none"><li>• Summary · BOQ · Sourcing</li><li>• Packing · Dispatch · Site</li><li>• Installation · Change orders</li><li>• Documents · Finance · Audit</li><li>• Cross-project dispatch board</li><li>• Damage &amp; shortage queue</li></ul></div> |
| <div><b>Installation</b></div> <div><code>/site</code></div> <div><ul style="list-style-type: none"><li>• My sites</li><li>• Incoming consignments + ETA</li><li>• Scan to receive, mark OK / damaged</li><li>• Install checklist by zone</li><li>• Snags in and out</li><li>• Request handover</li></ul></div>         | <div><b>Accounts</b></div> <div><code>/accounts</code></div> <div><ul style="list-style-type: none"><li>• Delivery challans</li><li>• E-way bill worksheet</li><li>• Tax invoices + credit notes</li><li>• Payments &amp; ageing</li><li>• Vendor bills, 3-way check</li><li>• Retention queue · GST export</li></ul></div> | <div><b>Client portal</b></div> <div><code>/portal</code></div> <div><ul style="list-style-type: none"><li>• All my showrooms, health dot</li><li>• Progress + site photos</li><li>• Scope at selling price</li><li>• Deliveries &amp; ETAs</li><li>• Approvals queue</li><li>• Sign handover · documents</li></ul></div>                                  |                                                                                                                                                                                                                                                                                                                                                                             |

06 — NOT IN THE ORIGINAL BRIEF

# Seven additions worth building first

These are not decoration. Each one closes a specific hole that is costing money or causing the complaints today.

|                      |                                                                                                                                                                                                               |
|----------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <div><b>01</b></div> | <div><b>BOQ kits — showroom presets</b></div> <div>Fifty near-identical showrooms. Clone a kit, adjust quantities, done. Project setup goes from hours to two minutes, and copy-paste errors disappear.</div> |
|----------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|

## 02 **Crate-level tracking with QR labels**

“Something did not arrive” is unanswerable at item level. Pack into crates, print a QR sticker, scan at dispatch and at site. Now you know *which crate*.

## 03 **Mandatory photos at packing and at receipt**

Settles every “it was already broken” argument, and tells you whether to claim from the transporter or fix the factory.

## 04 **Delivery Challan before Tax Invoice**

Goods move to site before the sale. Under GST that is a challan, not an invoice — with bill-to Ola HQ and ship-to the showroom. Getting this wrong invites notices.

## 05 **Site-readiness gate before dispatch**

Shipping to a site where flooring is not done means goods sit in a corridor and get damaged. Six checkboxes prevent the most expensive failure mode you have.

## 06 **Stale-status escalation**

If an item has not moved past its SLA, it surfaces automatically on two dashboards. Delay gets found in three days instead of three weeks.

## 07 **Replacement loop with costed rework**

A damaged item spawns a linked replacement that re-enters production and books its cost to the project, by cause. This is the silent margin killer made visible.

Three decisions are locked and written into the spec. The rest still need ten minutes with Kurchi.

DECIDED · PRICING

**“Actual price” = landed cost.** Four fields: base, selling, final agreed, and computed landed cost. Quoted margin and real margin both stored — the gap between them is the headline number.

DECIDED · CLIENT ACCESS

**Full portal in v1,** with BOQ approval, change orders and OTP handover signing. Field-level masking becomes a launch blocker, not later hardening.

DECIDED · GST

**Generate + export.** GST-correct challans and invoices, a complete e-way bill worksheet, GSTR-1-shaped export. No GSP subscription; the API route stays open.

OPEN · CLIENT USERS

**Which Ola people get logins?** One programme-level PM across all cities, or a site contact per showroom who only sees their own? Decides the user scoping model.

OPEN · INSTALLERS

**Third-party vendors or your own staff?** Decides whether the site app must be hardened for outsiders or can stay simple and trusting.

OPEN · ACCOUNTING

**Is Tally or Zoho already running?** If yes, the invoice number series must match theirs and this app exports rather than competes.

OPEN · CONTRACT

**Retention % and DLP months?** Assumed 5% and 12 months. And is billing milestone-based — advance, dispatch, completion — or one final invoice?

OPEN · STOCK

**Do you hold finished stock?** Or is everything made or bought per project? Decides whether a real inventory module is needed alongside make / buy.

OPEN · LANGUAGE

**Hindi or regional language on the site app?** Installers in tier-2 and tier-3 cities may not read English comfortably. Cheap now, painful to retrofit.

Full specification in `kurchi-projects/docs/` — overview, roles & permissions, workflow & 60+ business rules, screens, Firestore data model, roadmap, open questions. Stack: Vite · React · TypeScript · Tailwind · shadcn/ui · Firebase, matching `smart-furnish` and `ecommerce`.
